


# Raytown South High School Performing Arts Center & Aux Gym Addition WEEKLY PROGRESS REPORT 09/30/24

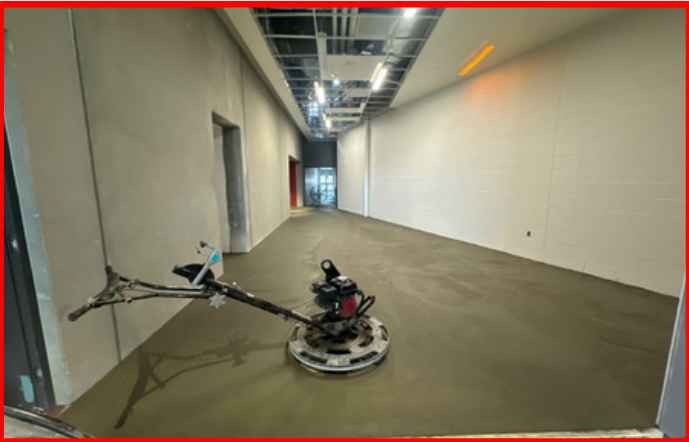

**Topping Slab**

**Last Week: 09/22/24 - 09/27/24**

- Exterior Signage at North Elevation
- Continue drilling/pouring piers in area B.
- Continue theatrical equipment install in stage.
- Topping slab in Pre-Function
- Cloud ceiling framing and sheetrock
- Paint flex auditorium ceiling
- Begin install of casework

**Next Week: 09/30/24 - 10/04/24**

- Digging and tying rebar for footings.
- Continue theatrical equipment install in stage.
- Asphalt paving.
- Continue pouring topping slab in Pre-Function
- Cloud ceiling framing and sheetrock
- Paint Scene Shop
- Drop ceiling tile

**Weather Days this week:**



**Cloud Ceilings**



**Casework Install**



**Pre-Function Lighting**
