

# Raytown South High School PAC and Auxiliary Gym WEEKLY PROGRESS REPORT 4/01/2024



Slab on Grade Poured at Scene Shop

### Last Week: 03/25 –03/29

- Structural steel and joist Install at auditorium and East entrance of building
- Placement of slab on grade at Scene Shop and Makeup/Dressing Areas
- Underground electrical rough in at main electrical room and Pre-Function areas
- Demobilization of precast crane
- Install of spiral stair

### Next Week: 04/01 –04/05


- Steel Decking Install at Scene Shop, Dressing/Makeup, and Auditorium
- Removal of Pre-Cast Braces
- Prep for slab on grade pours at south and west sides of Auditorium
- Prep for slab on grade pour at Pre-Function & Main Entrance
- CMU Install northeast side of Auditorium
- CMU Install at Dressing/Makeup area

### Weather Days this week:

(1) Monday 03/25



Steel Erection at Auditorium

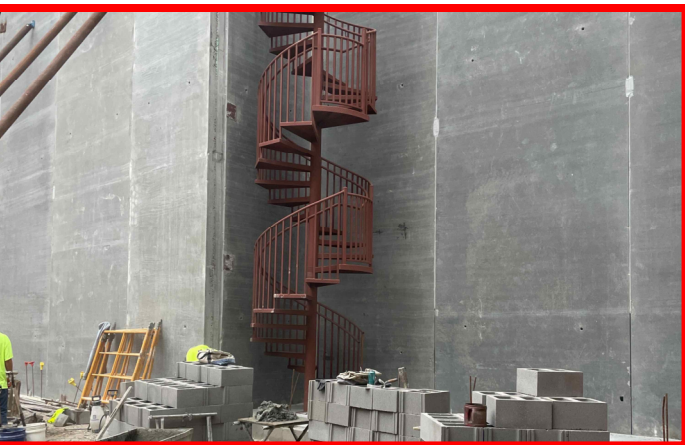

Install of Spiral Stair and Staging to Begin CMU Wall



Prior to Pour at Classroom/Dressing/Makeup Area
