

Raytown Quality Schools

MONTHLY PROJECT STATUS REPORT

JUNE 30, 2022

2022 Building Upgrades

Northwood, Laurel Hills, Spring Valley, Southwood, Little Blue Elementary

Demolition is complete at all locations

Installation of corridor floor tile is underway at Laurel Hills, Spring Valley, and Southwood

Northwood rough-ins for plumbing and electrical are complete with cabinetry installation planned for next week

Little Blue lighting replacements are in progress

Laurel Hills Media Center carpet installation is complete

Southwood Gym painting is completed

Raytown High School Renovation

Demolition is complete at all locations

New framing and rough-ins in the Media Center and FACs Room are underway

Corridor Flooring Replacements and painting are underway throughout

Raytown Central MS Renovation & Addition

Demolition is complete at all locations

New addition foundations have been dug and concrete poured. The exterior wall installation has started

New framing and rough-ins in the existing Cafeteria, Band, and Choir Rooms are underway

Corridor Flooring Replacements are underway throughout

Raytown South High School - Gym Stage Replacement

New framing has been completed and new subfloor plywood is being installed

New wood floor material has been delivered

Elementary Furniture Replacements

Installations have begun and are underway



Elementary Entry Graphic Installations & South HS Floor Stain

Installations are planned to begin in July.

Wellness Center Dedication Sign

Final design selections have been made, design drawings are being completed.

Raytown HS Choir Room Dedication Sign

Wording and design options are being reviewed.



Photographs




Laurel Hills Media Center



Northwood FACs Room



Southwood Gym

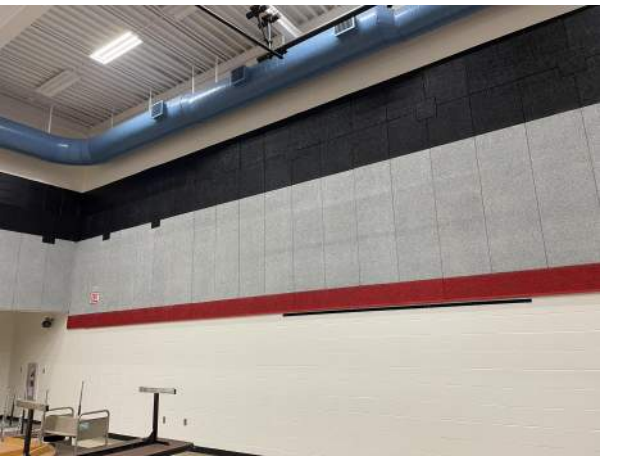

Photographs




Raytown High School, New Window Installation in Progress




Raytown High School, New Corridor Flooring



Raytown High School, New Cafeteria Floor Finish

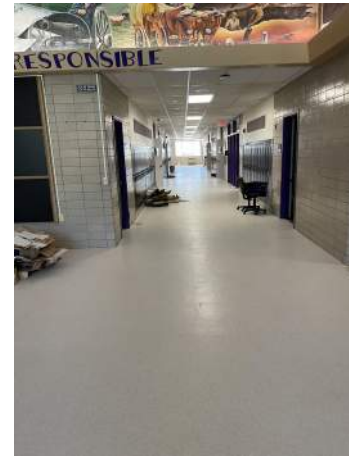

Central MS, New Corridor Floor Finish

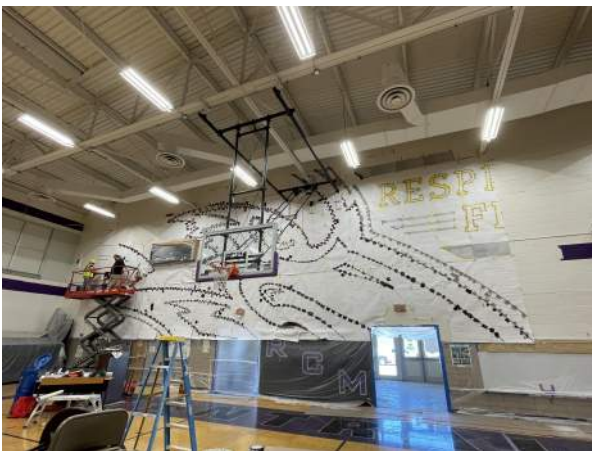

Central MS Gym Mural Paint Underway



Central MS, New Addition Foundation Installed

